



County Assessors Mapping Program

Status as of 4/15/03



Executive Summary

Detailed program status reports are posted to the Arkansas Geographic Information Office website once every month. The State Land Information Board and other major stake-holders are on an email distribution list that will contain a quick summary of the program status and a link to the detailed report on the website. For additional information, visit the County Assessors Mapping Program (CAMP) website at:

<http://www.gis.state.ar.us/AGIO/CAMP/status.htm>

Below is a list of County Assessors Mapping Program (CAMP) milestones:

- 57 counties have indicated they intend to join the CAMP program
- 50 of these Counties have returned a signed Memorandum Of Understanding (MOU) confirming their spot in the program.

Upcoming Events and Tasks

Here is an overview of some of the upcoming events for the CAMP program:

- AGIO has an outline drafted for State Cadastral Standards
- AGIO has requested points files from the Counties currently underway to check the linkage between the CAMA database and the points file.
- AGIO and AACD plan on meeting with CAMA providers to discuss standardization of CAMA database.
- 10 more Counties have taken the training. With 10 more to follow next week.

The following is a list of meetings that have taken place over the last month:

- Another 10 counties went through the training on March 5th - 7th.
- Traveled to Columbus, OH for the GIS/CAMA Conference.
- Spoke with Jen Grethen, Production manager of Promap, who will be converting Sebastian Counties Phase II data.
- Spoke with Jimmy West, Project Manager of Schneider Corp., who will be converting Benton Counties Phase II data.
- Spoke with Jen Grethen of ProMap, who will be converting Sabastian Counties Phase II data.

Status Overview

The 40 Counties that are underway are moving along smoothly. There have not been any major troubles as of yet. Another round of 10 Counties just finished the training and are beginning to create points file. With another 10 coming up a next week there will shortly be 50 counties entered into Phase I, with some well on their way to moving to Phase II. The AGIO has got a rough draft outline for the State Cadastral standards, and will be working to get a full rough draft together over the month.

Figure 1

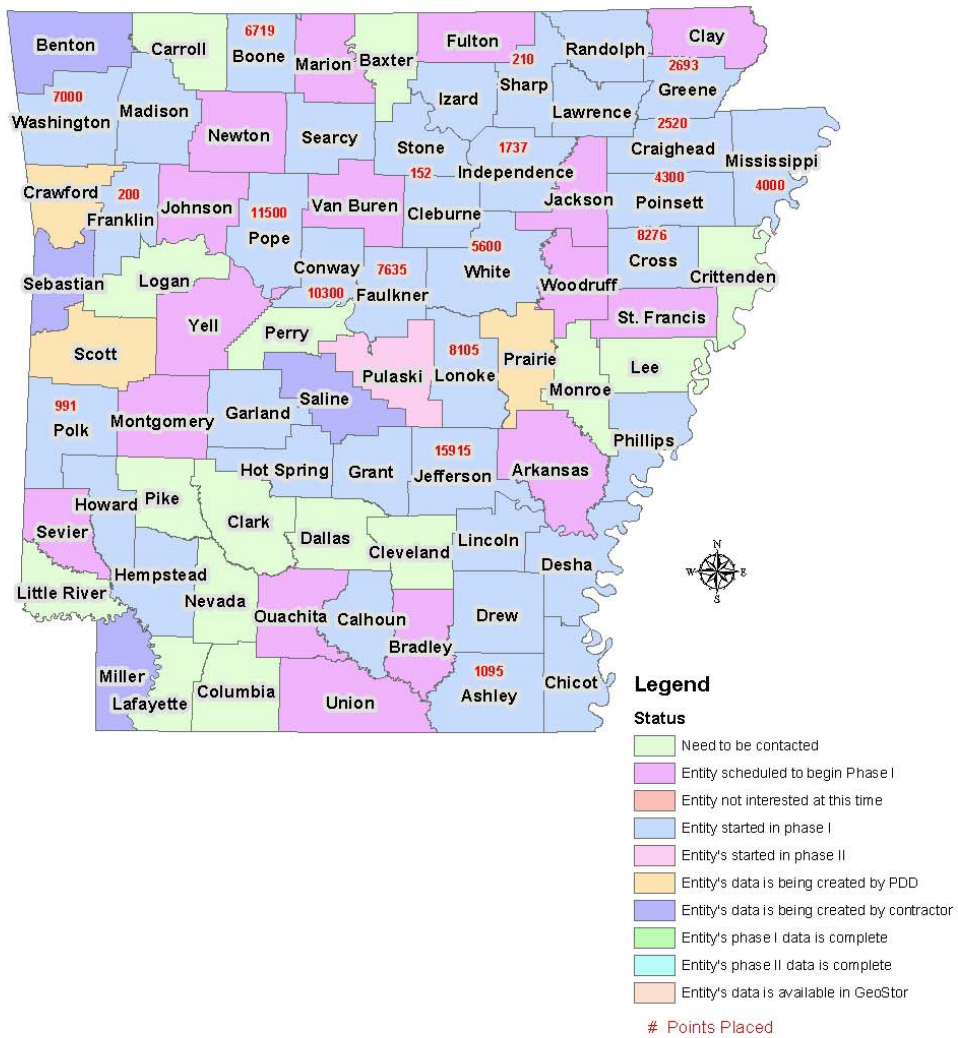


Table 1

County	Status	Status Date
Carroll County	Needs to be contacted	4/15/03
Cleburne County	County has begun Phase I	4/15/03
Greene County	County is currently working on Phase I and has 2693 points placed	4/15/03
Hot Spring County	County has begun Phase I	4/15/03
Izard County	County has begun Phase I	4/15/03
Lincoln County	County currently has points for CAMA entries, all that is required is adding the Parcel-id number and linking to CAMA database.	4/15/03
Lonoke County	County is well into Phase I with 8105 points captured	4/15/03
Madison County	County currently has points for each structure, all that is required is adding the Parcel-id and linking to the CAMA database.	4/15/03
Miller County	Counties Digital Cadastral data is being developed by a contractor.	4/15/03
Mississippi County	Started Phase I on 11/9/02 and has approximately 7% of Phase I completed	4/15/03
Nevada County	Needs to be contacted	4/15/03
Newton County	County is scheduled to enter Phase I on April, 23	4/15/03
Prairie County	County parcel data is being created by Planning and Development District	4/15/03
Pulaski County	County has started Phase II	4/15/03

Searcy County	County has begun Phase I	4/15/03
Washington County	Started Phase I, Has approximately 7000 points placed	4/15/03
Yell County	County is scheduled to begin Phase I	4/15/03
Arkansas County	County is scheduled to begin Phase I	4/15/03
Ashley County	County has begun Phase I and has approximately 1095 points placed.	4/15/03
Baxter County	County needs to be contacted	4/15/03
Benton County	Counties data is being captured by a contractor	4/15/03
Boone County	Started Phase I and has approximately 6719 points placed	4/15/03
Bradley County	Scheduled to begin Phase I on April, 23	4/15/03
Calhoun County	County has begun Phase I	4/15/03
Chicot County	County has started Phase I	4/15/03
Clark County	Needs to be contacted	4/15/03
Clay County	County is scheduled to begin Phase I on April 23	4/15/03
Cleveland County	Needs to be contacted	4/15/03
Columbia County	Needs to be contact.	4/15/03
Conway County	County began Phase I and has approximately 10300 points placed	4/15/03

Craighead County	County has started Phase I and has approximately 2520 points placed	4/15/03
Crawford County	County has begun Phase I	4/15/03
Crittenden County	Needs to be contacted	4/15/03
Cross County	County has started Phase I and has approximately 8276 points placed.	4/15/03
Dallas County	Needs to be contacted	4/15/03
Desha County	County has begun Phase I	4/15/03
Drew County	County has begun Phase I	4/15/03
Faulkner County	County started Phase I and has approximately 7635 points placed	4/15/03
Franklin County	County has started Phase I and has 200 points placed	4/15/03
Fulton County	County is scheduled to begin Phase I	4/15/03
Garland County	County has begun Phase I	4/15/03
Grant County	County has begun Phase I	4/15/03
Hempstead County	County has begun Phase I	4/15/03
Howard County	County has begun Phase I	4/15/03
Independence County	County has started Phase I and has 1737 points placed.	4/15/03
Jackson County	County is scheduled to begin Phase I on April 23	4/15/03

Jefferson County	County has started Phase I and has 15915 points placed	4/15/03
Johnson County	County is scheduled to begin Phase I	4/15/03
Lafayette County	County needs to be contacted	4/15/03
Lawrence County	County has begun Phase I	4/15/03
Lee County	Needs to be contacted	4/15/03
Little River County	Needs to be contacted	4/15/03
Logan County	Needs to be contacted.	4/15/03
Marion County	County is scheduled to begin Phase I	4/15/03
Monroe County	County is scheduled to begin Phase I on April 23	4/15/03
Montgomery County	County is scheduled to enter Phase I on April 23	4/15/03
Ouachita County	Needs to be contacted	4/15/03
Perry County	Needs to be contacted.	4/15/03
Phillips County	County has begun Phase I	4/15/03
Pike County	Needs to be contacted	4/15/03
Poinsett County	County has started Phase I and has 4300 points placed	4/15/03
Polk County	County has started Phase I and has 991 points placed	4/15/03

Pope County	County has begun Phase I and has 11500 points placed	4/15/03
Randolph County	County has begun Phase I	4/15/03
Saline County	County is scheduled to begin Phase I	4/15/03
Scott County	County data is being created by Planning and Development District	4/15/03
Sebastian County	County data being created by contractor	4/15/03
Sevier County	County is scheduled to begin Phase I	4/15/03
Sharp County	County has begun Phase I and has approximately 210 points placed	4/15/03
St. Francis County	County is scheduled to begin Phase I on April 23	4/15/03
Stone County	County has entered into Phase I and has 152 points placed	4/15/03
Union County	County is scheduled to begin Phase I	4/15/03
Van Buren County	County is scheduled to begin Phase I	4/15/03
White County	County has started Phase I and has 5600 points placed	4/15/03
Woodruff County	County is scheduled to begin Phase I on April 23	4/15/03
