



# County Assessors Mapping Program

## Status as of 7/15/03



### Executive Summary

Detailed program status reports are posted to the Arkansas Geographic Information Office website once every month. The State Land Information Board and other major stake-holders are on an email distribution list that will contain a quick summary of the program status and a link to the detailed report on the website. For additional information, visit the County Assessors Mapping Program (CAMP) website at:

<http://www.gis.state.ar.us/AGIO/CAMP/status.htm>

Below is a list of County Assessors Mapping Program (CAMP) milestones:

- Poinsett County successfully completed Phase I, has taken Phase II training and has begun building polygons.
- 62 counties have indicated they intend to join the CAMP program
- 60 of these Counties have returned a signed Memorandum Of Understanding (MOU) confirming their spot in the program.
- Attended ESRI Users Conference in San Diego, CA

### Upcoming Events and Tasks

Here is an overview of some of the upcoming events for the CAMP program:

- Washington County will be attending Phase II training on Aug 5<sup>th</sup>.
- I will be speaking at the Arkansas Society of Professional Surveyors meeting on Sept. 18<sup>th</sup>.
- AGIO has an outline drafted for State Cadastral Standards
- AGIO has requested points files from the Counties currently underway to check the linkage between the CAMA database and the points file.
- AGIO and AACD plan on meeting with CAMA providers to discuss standardization of CAMA database.
- We are currently looking at pilot counties to set up a direct connection between the ArcGIS points layer and the Windows based CAMA system.

The following is a list of meetings that have taken place over the last month:

- Met with Poinsett County for Phase II training.


## **Status Overview**

We have gotten 60 counties trained and started, with a few of these counties started in Phase II. Poinsett County has finished Phase I and has been trained and begun Phase II. This month has been a very busy one for the Assessors offices. The deadline for mailing out the Re-Appraisal Notices was this month and it has limited the activity on CAMP this month. A breakdown as to where each county stands is provided below. We are currently attempting to identify a county that will be the pilot for creating a 'live' link between the ArcGIS points file and the CAMA database. We are also in the final stages of creating a rough draft of the State Cadastral Mapping Standard.

For a breakdown of each county visit the new clickable map at:

[http://www.gis.state.ar.us/Downloads/GIS/camp/Clickable\\_map/Status\\_7\\_15\\_03.htm](http://www.gis.state.ar.us/Downloads/GIS/camp/Clickable_map/Status_7_15_03.htm)

Or see map below for a State wide overview:

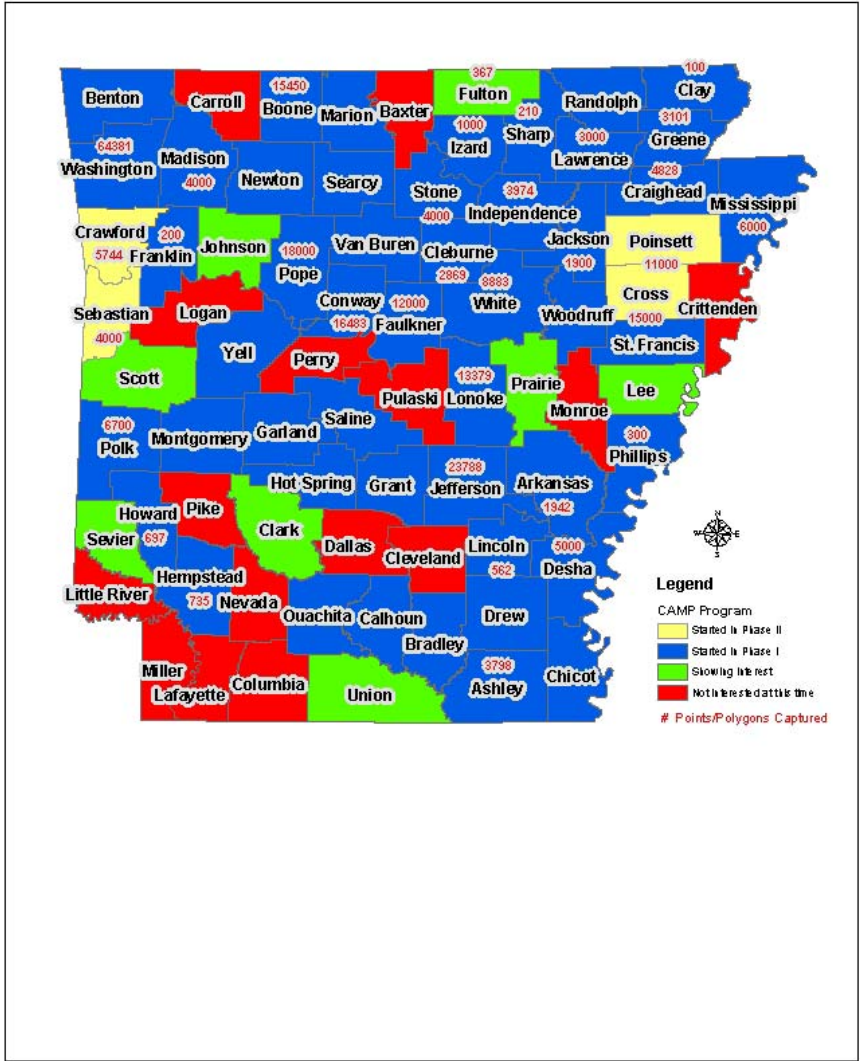

**Table 1**

Carroll County	Not interested at this time	7/15/03
Cleburne County	County took training in Jan. and has 2869 points placed	7/15/03
Greene County	County began Phase I in Nov. 2002 and has 3101 points placed.	7/15/03
Hot Spring County	County took training in Mar. 2003 and has just received hardware and software.	7/15/03
Izard County	County began Phase I in Mar. 2003 and has 1000 points placed	7/15/03
Lincoln County	County took training for Phase I in Mar. 2003 and points for CAMA entries were created by another entity, all that is required is adding the Parcel-id number and linking to CAMA database. 562 points currently placed by the county.	7/15/03
Lonoke County	County began Phase I in Nov 2002 and has 13379 points captured	7/15/03
Madison County	County began Phase I in Mar. 2003 and has 4000 points placed	7/15/03
Miller County	Counties Digital Cadastral data is being developed by a contractor.	7/15/03
Mississippi County	Started Phase I on Nov. 2003 and has 6000 points placed	7/15/03
Nevada County	Not interested at this time	7/15/03
Newton County	County has taken Phase I training but is currently waiting to receive hardware and software.	7/15/03
Prairie County	County parcel data is being created by Planning and Development District	7/15/03
Pulaski County	Not interested at this time	7/15/03

Searcy County	County has started Phase I	7/15/03
Washington County	County began Phase I in Jan. 2003, and coordinating with the City of Fayetteville and the City of Springdale they have captured 64,381 points. And has started Phase II	7/15/03
Yell County	County took training in April 2003, but is waiting for hardware and software to arrive.	7/15/03
Arkansas County	County has started Phase I and has 1942 points placed	7/15/03
Ashley County	County began Phase I in Mar. 2003 and has captured 3798 points	7/15/03
Baxter County	Not interested at this time	7/15/03
Benton County	County took Phase I training in Jan. 2003, they are receiving deliveries from contractor and doing Quality Control of data.	7/15/03
Boone County	County started Phase I in Jan. 2003 and has 15450 points captured	7/15/03
Bradley County	County took Phase I training in Mar. 2003, has received software and hardware but has yet to begin capturing points.	7/15/03
Calhoun County	County took Phase I training in Mar. 2003 and is waiting for hardware and software to be delivered.	7/15/03
Chicot County	County took Phase I training in Jan. 2003 and has yet to start capturing points.	7/15/03
Clark County	County has begun Phase I	7/15/03
Clay County	County began Phase I in Mar. 2003 and has 100 points placed	7/15/03
Cleveland County	Not interested at this time	7/15/03
Columbia County	Not interested at this time	7/15/03
Conway County	County began Phase I in Nov. 2002 and has captured 16483 points	7/15/03

Craighead County	County began Phase I in Jan. 2003 and has approximately 4828 points placed.	7/15/03
Crawford County	County has begun Phase II and has 5744 parcel polygons built.	7/15/03
Crittenden County	Not interested at this time	7/15/03
Cross County	County started Phase I in Nov. 2003 and has 15000 points placed. Has completed Phase I and has begun Phase II	7/15/03
Dallas County	Not interested at this time	7/15/03
Desha County	County took training in Mar. 2003 and has 5000 points placed.	7/15/03
Drew County	County has begun Phase I	7/15/03
Faulkner County	County started Phase I in Nov. 2003 and has approximately 12000 points placed	7/15/03
Franklin County	County started Phase I in Jan. 2003 and has 200 points placed	7/15/03
Fulton County	County has started Phase I and has 367	7/15/03
Garland County	County has begun Phase I	7/15/03
Grant County	County took training in Mar. 2003 and is waiting for software to be delivered.	7/15/03
Hempstead County	County took training in Mar. 2003, and has 735 points placed	7/15/03
Howard County	County took Phase I training in Mar., and has 697 points placed.	7/15/03
Independence County	County began Phase I in Jan. 2003 and has 3974 points placed.	7/15/03
Jackson County	County began Phase I in Mar. 2003 and has captured 1900 points.	7/15/03

Jefferson County	County began Phase I in Nov. 2002 and has 23788 points placed	7/15/03
Johnson County	County has begun Phase I	7/15/03
Lafayette County	Not interested at this time	7/15/03
Lawrence County	County began Phase I in Mar. and has 3000 points placed	7/15/03
Lee County	Not interested at this time	7/15/03
Little River County	Not interested at this time	7/15/03
Logan County	Not interested at this time.	7/15/03
Marion County	County has begun Phase I	7/15/03
Monroe County	County is scheduled to begin Phase I	7/15/03
Montgomery County	County has begun Phase I	7/15/03
Ouachita County	County has begun Phase I	7/15/03
Perry County	Not interested at this time	7/15/03
Phillips County	County began Phase I in Mar. 2003 and has 300 points placed.	7/15/03
Pike County	Not interested at this time	7/15/03
Poinsett County	County has begun Phase II	7/15/03
Polk County	County started Phase I in Jan. 2003 and has 6700 points placed	7/15/03

Pope County	County began Phase I and has 18000 points placed	7/15/03
Randolph County	County took Phase I training in Mar. 2003 and has yet to start capturing points.	7/15/03
Saline County	County has begun Phase I	7/15/03
Scott County	County is scheduled to begin Phase I in June, point data is being created by an outside entity.	7/15/03
Sebastian County	County began Phase I in Jan. 2003 and is talking with contractors to create data.	7/15/03
Sevier County	County is scheduled to begin Phase I	7/15/03
Sharp County	County began Phase I in Nov. 2002 and has approximately 210 points placed	7/15/03
St. Francis County	County has taken Phase I training and is waiting to hire employee for program.	7/15/03
Stone County	County entered into Phase I in Mar. 2003 and has 4000 points placed	7/15/03
Union County	County is scheduled to begin Phase I	7/15/03
Van Buren County	County has begun Phase I	7/15/03
White County	County started Phase I in Nov. 2002 and has 8632 points placed	7/15/03
Woodruff County	County has begun Phase I	7/15/03
